

Product Roadmap & MVP Strategy

MyCCAngel

Version: 1.0

Product Lead: Baqer [Last Name]

Project Duration (planned): Initial MVP, 4–6 months

Note: This document is preserved as originally written at project kickoff. It reflects the planning and prioritization thinking at the start of the project, not the current build status. For current status of each feature, see the companion PRD and Case Study documents.

1. Product Vision

Vision Statement

To build a trusted AI-powered digital platform that empowers individuals living with Inflammatory Bowel Disease (IBD) by connecting them with a supportive community, personalized resources, and intelligent tools that improve their daily lives.

Our long-term vision is to become the leading global digital ecosystem for IBD patients, healthcare professionals, and partner organizations.

2. Product Objectives

The initial objective is not to build every planned feature.

Instead, the objective is to deliver a functional Minimum Viable Product (MVP) that demonstrates the platform's value, validates user interest, and enables discussions with healthcare organizations, clinicians, potential partners, and investors.

The MVP should allow us to:

- Demonstrate the complete user journey
- Validate the product concept with real users
- Begin acquiring an initial user base
- Collect user feedback
- Secure partnerships with IBD organizations and healthcare professionals
- Position the project for future funding opportunities

3. Product Principles

Every feature added to MyCCAngel should support at least one of the following principles.

Build Trust

Users should feel confident they are interacting with a genuine community of IBD patients.

Deliver Immediate Value

New users should benefit from the platform immediately after registration.

Personalize the Experience

The platform should adapt to each patient's profile and needs.

Keep the MVP Simple

Only build features required to validate the product vision.

Design for Growth

Every feature should support future expansion without requiring significant redesign.

4. MVP Scope

The first release focuses on building a functional platform rather than a fully featured ecosystem.

Included Features

User Management

- User Registration
- Login & Authentication
- Password Reset
- User Profiles

Patient Verification

- Medical Report Upload
- OCR Processing
- AI Classification Model
- Verification Workflow

Purpose: Create a trusted patient community by verifying that new users have an IBD diagnosis.

Personalized Onboarding

Users complete an onboarding questionnaire capturing:

- Age, Gender, Country
- Disease Type, Years Since Diagnosis
- Symptom Severity, Daily Challenges
- Interests, Support Needs

Initially, this data will power simple rule-based recommendations and establish a foundation for more advanced personalization as the user base grows.

Recommendation Engine (Version 1)

The recommendation system will initially recommend:

- Similar users (where possible)
- Educational articles, documents, and resources

Due to the cold-start problem, recommendations will primarily rely on onboarding survey responses and user profile attributes. As user activity increases, future versions will incorporate behavioral data such as article views, group participation, searches, and interactions.

Community

- User Profiles
- Direct Messaging

Community feeds, posts, and groups will remain limited during the MVP phase until a sufficient user base has been established.

Resource Library

A structured resource library containing educational articles and IBD management documents. The framework for future partner-contributed resources will also be included, even if directories are initially empty.

AI Chatbot (Version 1)

An AI-powered chatbot capable of answering common IBD questions, explaining educational content, and guiding users to platform resources. The chatbot will not provide diagnoses or treatment recommendations.

Toilet Locator

Allow users to locate nearby public toilets using location services. This feature addresses one of the most frequently reported daily challenges faced by IBD patients.


5. Features Excluded from the MVP

The following features are planned but intentionally postponed until after product validation:

- Doctor Directory, Dietitian Directory, Partner Organization Portal
- Community Posts, Community Groups, Events, Volunteer Portal
- Donations, Restaurant Recommendations
- Advanced AI Personalization, Symptom Tracking, Medication Tracking

These features depend on partnerships, user growth, or additional research.

6. Product Roadmap

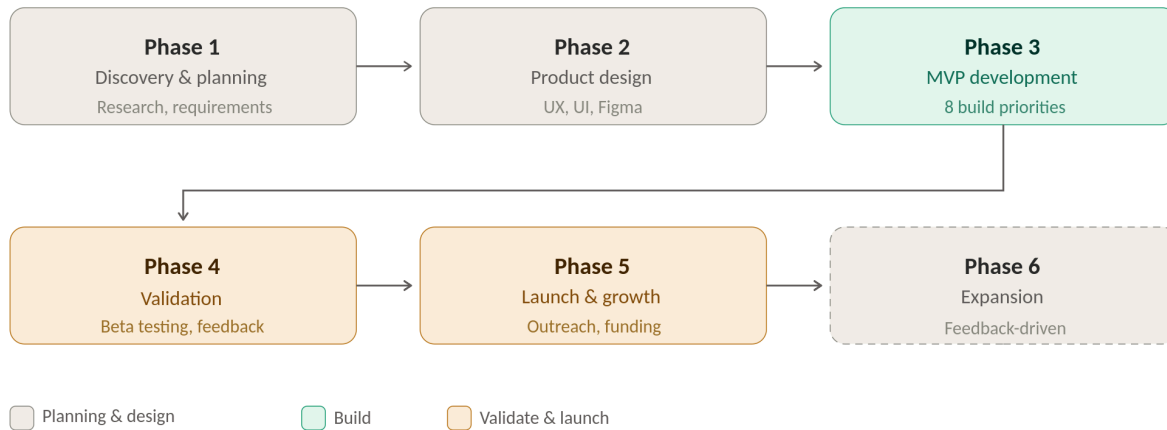

Phase 1 — Discovery & Planning

Goal: Define the product vision, user needs, and technical requirements.

Key Activities:

- Market Research, User Research, Patient Survey Design
- Product Requirements, Technology Selection, Database Design
- Roadmap Development, Team Formation

Deliverables: Product Vision, Roadmap, Survey, Technical Architecture

Phase 2 — Product Design

Goal: Design a user-centered experience before development begins.

Key Activities:

- User Journey Mapping, Information Architecture
- Wireframes, UX Design, UI Design
- Figma Prototypes, Design Reviews

Deliverables: Complete Figma Designs, User Flows, Platform Branding, Design System

Phase 3 — MVP Development

Goal: Build a working platform demonstrating the complete product vision.

Development Priorities (in order):

- Priority 1 — User Registration, Authentication, User Profiles
- Priority 2 — Medical Report Verification
- Priority 3 — Onboarding Questionnaire
- Priority 4 — Recommendation Engine
- Priority 5 — Resource Library
- Priority 6 — Direct Messaging
- Priority 7 — AI Chatbot
- Priority 8 — Toilet Locator

Deliverables: A fully functional MVP suitable for demonstrations and early user testing.

Phase 4 — Validation

Goal: Validate assumptions using real users.

Activities:

- Internal Testing, Beta Testing, User Interviews
- Bug Fixes, UX Improvements, Performance Optimization

Success Criteria:

- Users complete onboarding successfully
- Medical verification functions reliably
- Users understand the platform
- Positive qualitative feedback

Phase 5 — Launch & Early Growth

Goal: Begin growing the community while securing strategic partnerships.

Activities:

- Launch MVP, Marketing Campaigns
- Patient Recruitment, Organization Outreach, Doctor Outreach
- Funding Discussions

Objectives:

- Acquire early users, collect product feedback
- Build credibility, demonstrate traction

Phase 6 — Product Expansion

Expansion priorities will be determined based on user feedback and platform analytics. Potential additions include:

- Community Feed, Posts & Comments, Interest Groups, Events
- Doctor Directory, Dietitian Directory, Partner Organizations, Restaurant Finder
- Advanced Recommendation Engine, Research Participation
- Symptom Tracker, Medication Tracker

7. Success Metrics

The MVP will be evaluated using qualitative and quantitative metrics.

User Acquisition

- Number of Registrations
- Registration Completion Rate
- Medical Verification Success Rate

User Engagement

- Daily Active Users, Weekly Active Users
- Average Session Duration

AI Metrics

- Medical Report Classification Accuracy
- Recommendation Click-Through Rate
- Chatbot Usage

Validation Metrics

- User Feedback, Patient Satisfaction
- Organization Interest, Partnership Discussions

8. Risks & Mitigation

Risk	Mitigation
Limited development resources	Prioritize only essential MVP features
Small user base	Focus on validating the concept before scaling
Cold-start recommendation problem	Use onboarding survey data until behavioral data becomes available
Limited healthcare partnerships	Build a demonstrable platform before approaching organizations
Funding constraints	Use the MVP to support grant applications, partnerships, and investor discussions

9. Long-Term Product Vision

The MVP is only the first step toward a much broader healthcare ecosystem. Future versions of MyCCAngel aim to include:

- Verified healthcare professional directories
- Community-driven support groups
- Personalized AI recommendations based on user behavior
- Research participation opportunities
- Healthcare organization partnerships
- Educational events
- Advanced patient management tools
- AI-powered health insights

By validating the MVP first, the team can prioritize future development based on real user needs rather than assumptions.
